

Construction crews move forward with foundation, electrical and other work

Latest Information

Completed this week:

1. Underground electrical and plumbing south pod
2. Base rock south pod
3. North pod exterior masonry
 - Setting steel and deck on the east pod will be completed Nov. 20.
 - Base rock on north pod will be completed Nov. 20.
 - Installation of exterior plywood is ongoing.
 - Underground electrical and plumbing on the north pod will be completed Nov. 20.
- Tentatively, concrete pours will begin on the east pod Nov. 30, on the north pod Nov. 23, and on the south pod Nov. 16.
- Roofing on the north pod will be completed on Nov. 18 and on the south pod on Dec. 4.
- Installation of the sky light curbs and parapet cap will be completed Nov. 19.
- Installation of air barrier will be completed Nov. 18.
- Installation of exterior plywood is ongoing.
- Installation of brick veneer will begin Nov. 16.



Crews work on the Flexible Industrial Technology building. Ty Stockton/LCCC

FLEXIBLE INDUSTRIAL TECH BUILDING

- Exterior metal stud framing will begin Nov. 16.
- Exterior rigid insulation will be completed Nov. 20.
- Tentatively, slab on deck will begin Dec. 3.

Project Cost/Details


The \$16 million, 46,000-square-foot building is projected to open in fall 2016. The new building will be home to Diesel Technology, Engineering Technology, expanded Welding Fabrication program, Construction Management, Process Technology and will provide room for expansion of other budding programs. The general contractor is FCI Constructors.

Latest Information

Completed this week:

1. Backfill basement walls
2. Rammed aggregate piers at basement walls
3. Finish foundation excavation
4. Building electrical feed under foundations
5. Tunnel racking/piping/insulation
 - Foundation work including insulation and backfill will finish by Dec. 1.
 - Construction of steel structures on Area B (east side) will be ongoing.
 - Construction of steel structures on Area A (west side) and tie-in to Area B will begin Nov. 30.
 - Exterior metal stud framing Area B (east side) will begin Dec. 14.
 - Winter enclosure over studs will begin Dec. 16.
 - Basement overhead mechanical, electrical and plumbing underground work will begin Nov. 9 and will be ongoing.
 - Tentatively, Floor 2 slab on deck will begin Dec. 21.
 - Foundation sleeves/grounding will be completed Nov. 20.
 - Potential utility tie-ins across sidewalk will occur Nov. 28.

STUDENT SERVICES/ UNIVERSITY CENTER

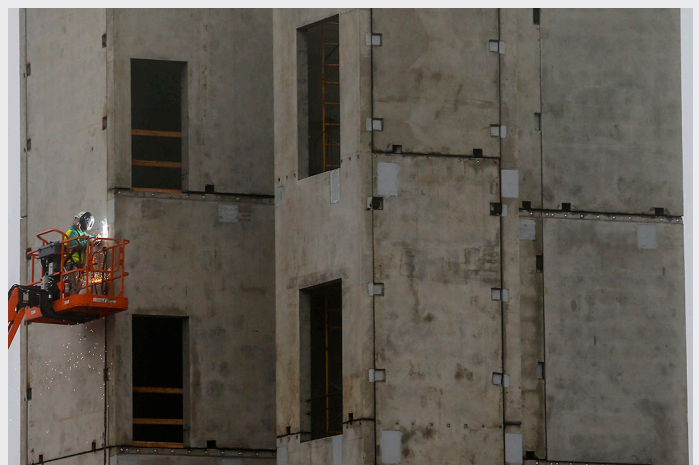

Crews work on the Student Services/University Center. Michael Smith/LCCC

Project Cost/Details

The \$30 million, 85,000-square-foot building is projected to open its doors in spring 2017. The building will be home to several departments including Admissions, LCCC Bookstore, Student Records, Financial Aid, Counseling & Campus Wellness, Disability Services, Advising and Career Services and University of Wyoming Outreach. It will provide classroom, office and assembly space. The general contractor is FCI Constructors.

Parking and Getting Around

Visit LCCC's website at lccc.wy.edu, and click on the Construction Update section for the latest information about parking.

Note: Only those who have business on the project construction sites are allowed on the sites (behind the fence). These individuals are required to check in with the contractor at the construction trailer and must wear the necessary protective and safety gear.
